Chevron

Gorgon Project Master Schedule 3 x 5 mtpa

Printed : 15-Oct-09 08:57
User : mjyj

D&C - CONTRACTS ONLY - TENDER PERIOD ONLY

Activity Name	Owner	Contract Advisor	Activity % Complete	Start	Finish
Cement and Services - Tender Period	J. Gauld	L. Fimmel	100%	16-Oct-08 A	26-Nov-08 A
CRA Tubular - Tender Period	F. Smits	N. Michael	100%	15-Jun-09 A	29-Jul-09 A
OCTG, Carbon Steel Tubulars - Tender Period	F. Smits	N. Michael	100%	15-Jun-09 A	29-Jul-09 A
ROV and Services - Tender Period	Ben Goddard	D. Davies	100%	17-Jun-09 A	22-Jul-09 A
Flow Control - Tender Period	S. Monro	T. Creaven	100%	03-Aug-09 A	14-Sep-09 A
Safety Valve - Tender Period	A. Azuara	L. Nissen	100%	03-Aug-09 A	14-Sep-09 A
Liner Hangers - Tender Period	S. Monro	T. Creaven	100%	03-Aug-09 A	14-Sep-09 A
Sub-Assembly Workshop - Tender Period	S. Monro	T. Creaven	100%	03-Aug-09 A	14-Sep-09 A
Permanent Downhole Gauges - Tender Period	A. Azuara	L. Nissen	100%	03-Aug-09 A	14-Sep-09 A
WT - Heat Suppression - Tender Period	Rafael Ramirez	N. Michael	0%	21-Sep-09	13-Nov-09
Casing & Tubing Running Tools - Tender Period	T. Jobin	D. Davies	0%	28-Sep-09	20-Nov-09
Slickline - Tender Period	S. Monro	L. Fimmel	0%	02-Nov-09*	08-Jan-10
WT - Surface Well Testing - Tender Period	Rafael Ramirez	N. Michael	0%	02-Nov-09*	08-Jan-10
WT - SSTT and SFT - Tender Period	Ben Goddard	N. Michael	0%	02-Nov-09*	08-Jan-10
Casing Accessories - Tender Period	F. Smits	N. Michael	0%	12-Jan-10	08-Mar-10
Suspension Packer - Tender Period	A. Azuara	D. Davies	0%	22-Feb-10	09-Apr-10
Open Hole Electricline - Tender Period	T. O'Connell	L. Nissen	0%	01-Mar-10	30-Apr-10
D&C Fluids Services & Materials - Tender Period	M. Fernau	L. Fimmel	0%	01-Mar-10	30-Apr-10
DD, MWD and LWD - Tender Period	J. Buchan	T. Creaven	0%	01-Mar-10	30-Apr-10
Cased Hole Electricline & Perf. - Tender Period	C. Oudtshoorn	L. Fimmel	0%	01-Mar-10	30-Apr-10
Rig & Rotary Inspection Services - Tender Period	M.Cavanaugh	N. Michael	0%	10-Mar-10	11-May-10
Inspections & Prep Casing & Tubing - Tender Period	F. Smits	N. Michael	0%	15-Mar-10	14-May-10
Mud Logging Services - Tender Period	B. Halders	L. Fimmel	0%	07-Apr-10	01-Jun-10
Rig Positioning Services - Tender Period	G. Crane	N. Michael	0%	19-Apr-10	11-Jun-10
Solids Control Equip and Services - Tender Period	M. Fernau	L. Fimmel	0%	19-Apr-10	11-Jun-10
Well Clean Up Tools - Tender Period	S. Monro	D. Davies	0%	20-Apr-10	14-Jun-10
Fishing Services - Tender Period	C. Coning	D. Davies	0%	04-May-10	28-Jun-10
Drilling Rental Tools - Tender Period	C. Coning	D. Davies	0%	04-May-10	28-Jun-10
Machine Shop - Tender Period	C. Coning	D. Davies	0%	11-May-10	05-Jul-10
Drill Bits - Tender Period	W. Metcalf	D. Davies	0%	22-Jun-10	16-Aug-10
PDC Underreamer - Tender Period	W. Metcalf	D. Davies	0%	22-Jun-10	16-Aug-10

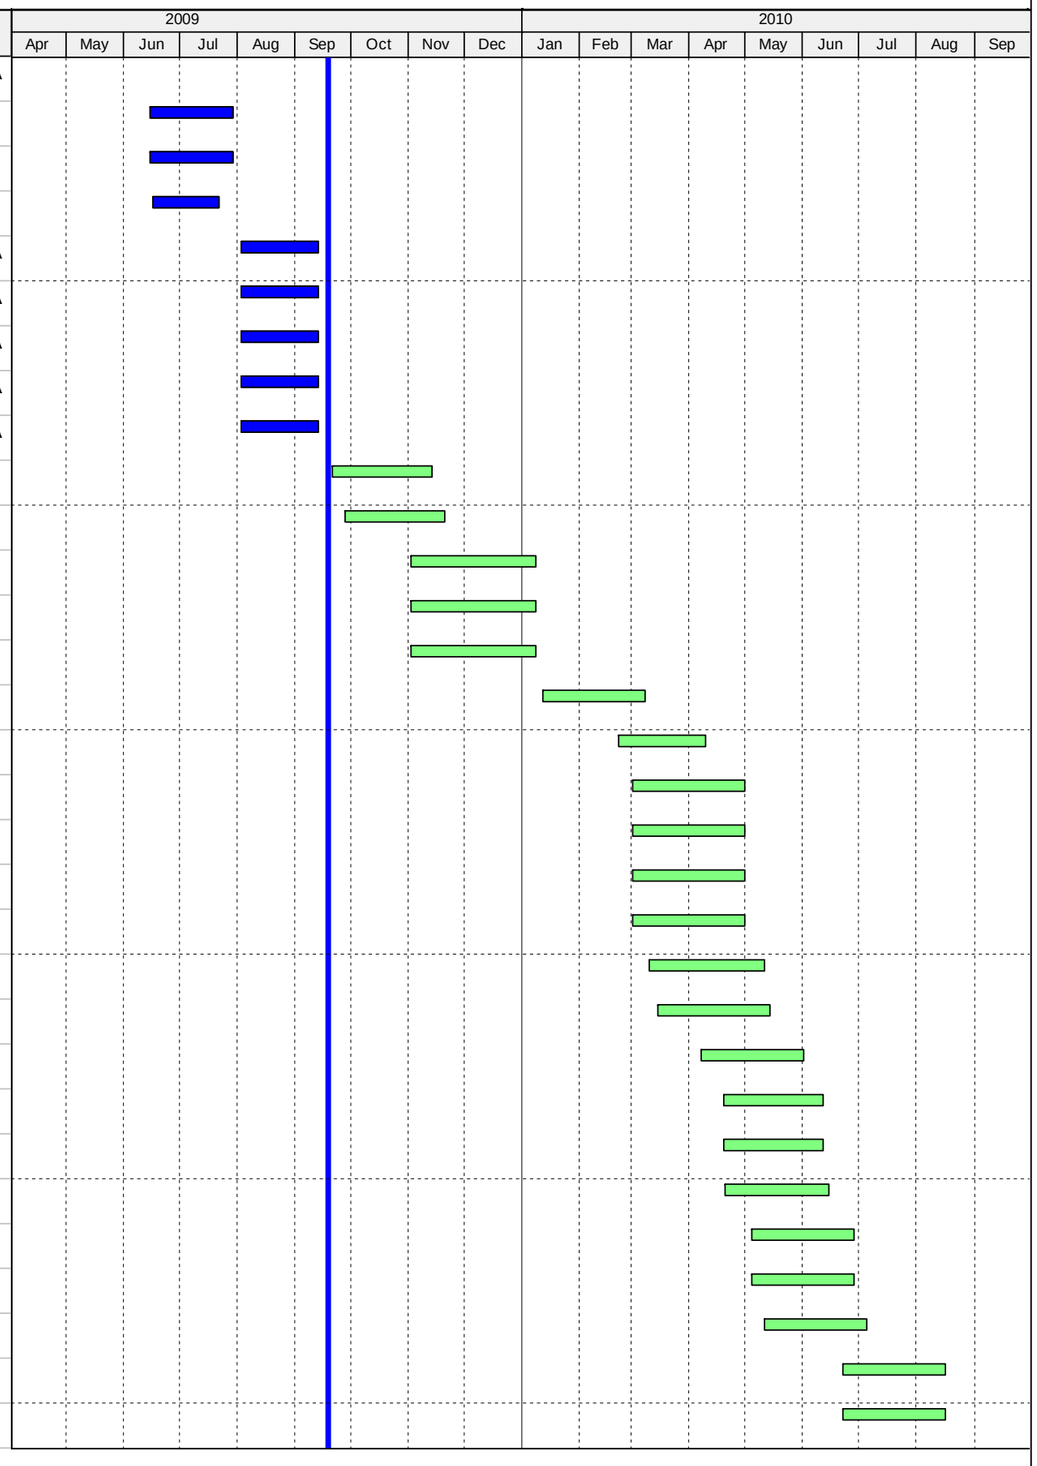

Filter: TASK filter: RFP Filter.
Layout:Gorgon Contracts Tender Period Activitie Data Date:19-Sep-09
Baseline:

Remaining Work
Actual Work
Summary
Critical Remaining Work
Milestone
